

Sensory Room Refurbishment

Full Project Plan — Dame Hannah Rogers Trust

Organisation	Dame Hannah Rogers Trust
Location	Woodland Road, Ivybridge, PL21 9HQ
Internal Contact	Wayne Fulton
Primary Contractor	So Sensory (kevin.phillips@sosensory.com)
Document Version	1.0 (Draft)
Date	March 2026
Status	⚠ Pending Gap Resolution & Board Approval

£16,560	~£20–25k	~12 wks	25
KNOWN QUOTED COST	ESTIMATED FULL COST	PROJECT DURATION	GAPS IDENTIFIED

Sensory Room Refurbishment — Full Project Plan

Organisation: Dame Hannah Rogers Trust
Location: Woodland Road, Ivybridge, PL21 9HQ
Internal Contact: Wayne Fulton
Document Version: 1.0 (Draft)
Date: March 2026

Contents

1. Executive Summary
 2. Project Scope
 3. Known Information — What We Have
 4. Financial Breakdown — All Quotations Collated
 5. Contractor Breakdown
 6. In-House vs Contractor Work
 7. Project Timeline — Gantt Chart
 8. Funding Breakdown
 9. Risk Register
 10. Gaps — What We Don't Know and Need to Find Out
 11. Next Steps & Action List
-

1. Executive Summary

Dame Hannah Rogers Trust is planning to refurbish its existing sensory room using donation funding. Three quotations have been received from **So Sensory** (the primary specialist contractor) covering sensory equipment and technology upgrades, HD projection equipment, and new floor and wall padding. An estimate has also been received for covering a Vibro Acoustic Platform (VAP), to be carried out by sub-contractor **Tugboat & Dolphins** in Plymouth.

Based on the quotations received to date, the **known project cost is approximately £16,560**. However, several areas of work (electrical, structural, decoration, project management, contingency, and VAT treatment) are not yet costed, meaning the full project cost is unknown.

This document collates all available data, maps out the proposed works, identifies the contractor and in-house effort, provides a draft project timeline, and — critically — **lists all the information gaps that must be resolved before the project can be formally approved and started.**

2. Project Scope

The project involves the full refurbishment and upgrade of the existing sensory room to create an enhanced, future-proofed therapeutic and recreational space for residents and users of Dame Hannah Rogers Trust.

Scope Includes (confirmed from quotations):

Ref	Work Area	Contractor
S1	Design, supply & install new sensory lighting and interactive equipment	So Sensory
S2	Supply & install HD Ultra Short Throw Projector, Apple TV, router and cabling	So Sensory
S3	Design, supply & deliver new floor and wall padding (extended floor, raised wall panels)	So Sensory
S4	Cover Vibro Acoustic Platform (VAP) with foam, including removeable top / access panel	Tugboat & Dolphins (via So Sensory)

Scope Likely Required but NOT Yet Confirmed:

Ref	Work Area	Notes
U1	Electrical works (new circuits, sockets, dedicated circuits for equipment)	To be confirmed — electrical contractor needed
U2	Structural/building works (walls, ceiling, doors)	Assess room condition first
U3	Painting and decoration	Possibly in-house
U4	Removal and disposal of existing equipment/furnishings	Cost unknown
U5	IT / Network infrastructure (WiFi, router, network point)	Partially covered by So Sensory quote
U6	iPad/tablet provision for Bluetooth control	Assumed available in v3.0 quote — to confirm
U7	VAP shipping (from Ivybridge to Bristol factory and back)	Logistics to be arranged
U8	Snagging and final sign-off inspection	TBC

3. Known Information — What We Have

3.1 Quotations Received

All three quotations from **So Sensory** are dated **18 March 2026** and addressed to **Wayne Fulton, Dame Hannah Rogers Trust**.

Quote 1 — Sensory Equipment Upgrade (Ref: 180326)

Upgrade the existing sensory room with new lighting, interactive devices and control infrastructure.

Item	Qty	Unit Cost	Total
Chromatube+ with remote control	1	£1,450.00	£1,450.00
Corner plinth, back board and mirrors	2	£950.00	£1,900.00
Laser Lights	2	£80.00	£160.00
Fibre Optic Strands with LED light source	1	£500.00	£500.00
Galaxy Star Projector and wall mount (remote control)	1	£215.00	£215.00
Mirror ball and spotlight and motor	1	£185.00	£185.00
UV LED Light Bar	2	£80.00	£160.00
UV reactive stars and hanging solar system	1	£95.00	£95.00
LED surround lighting with remote control	1	£395.00	£395.00
Bluetooth Switching	10	£60.00	£600.00
Bluetooth bridge	1	£120.00	£120.00
Wifi/ethernet adapter	1	£120.00	£120.00
Labour (days)	7	£375.00	£2,625.00
Sub Total			£8,525.00
Deposit (50%)			£4,262.50
Final Payment			£4,262.50

Note: Quote assumes an iPad/tablet is available for the room and that permissions for software to be loaded onto it are granted.

Quote 2 — HD Projector (Ref: 210326)

Supply and install a HD wall-mounted projector with media streaming capability.

Item	Qty	Unit Cost	Total
Apple TV, router and cabling	1	£500.00	£500.00
HD Ultra Short Throw Projector & Wall Mount	1	£1,995.00	£1,995.00
Sub Total			£2,495.00
Deposit (50%)			£1,247.50
Final Payment			£1,247.50

Note: Includes 5-year full-service warranty with scheduled annual servicing and door-to-door collection & return service for technical issues.

Quote 3 — Floor and Wall Padding (Ref: 200326)

Design, supply and deliver all floor and wall padding to the sensory room.

Item	Qty	Unit Cost	Total
Floor and wall pads (per drawings), including extended floor by 1200mm full width and wall panels raised to 1500mm	1	£5,000.00	£5,000.00
Sub Total			£5,000.00
Deposit (50%)			£2,500.00
Final Payment			£2,500.00

Estimate — Vibro Acoustic Platform (VAP) Covering (Ref: E190326)

Covering of a pre-constructed VAP with foam, to be carried out by Tugboat & Dolphins, Plymouth.

Item	Qty	Unit Cost	Total
Covering with removeable top (recommended — allows access to amplifier)	1	£540.00	£540.00
OR Covering as a single wrap	1	£405.00	£405.00
Sub Total (preferred option)			£540.00

Note: All electronics must be removed from the VAP prior to shipping to the Bristol factory. Shipping costs are **not included** in this estimate and need to be costed separately.

3.2 Design Drawings

3D representation drawings for the sensory room refurbishment have been produced (March 2026) and are held in the file "**Dame Hannah Rogers Trust 3D Dwgs.pdf**". These consist of a cover page and four pages of visual drawings showing the proposed layout and design.

4. Financial Breakdown — All Quotations Collated

4.1 Summary of Known Costs

Ref	Description	Contractor	Cost (£)	Status
Q1	Sensory equipment upgrade (lighting, fibre optics, Bluetooth controls, labour)	So Sensory	£8,525.00	Quote received
Q2	HD Ultra Short Throw Projector, Apple TV, router and cabling	So Sensory	£2,495.00	Quote received
Q3	Floor and wall padding (extended floor + raised panels)	So Sensory	£5,000.00	Quote received
Q4	VAP foam covering (removeable top option)	Tugboat & Dolphins	£540.00	Estimate received
Total — Confirmed Quotes			£16,560.00	

4.2 Payment Schedule (Confirmed Quotes)

All So Sensory quotes require a **50% deposit on acceptance** with the **balance on completion**.

Ref	Deposit (50%)	Final Payment	Total
Q1	£4,262.50	£4,262.50	£8,525.00
Q2	£1,247.50	£1,247.50	£2,495.00
Q3	£2,500.00	£2,500.00	£5,000.00
Q4	TBC	TBC	£540.00
Total	£8,010.00	£8,010.00	£16,560.00

Payment details for So Sensory: NatWest — Sort Code: 56 00 63 — Account No: 46507612

4.3 Costs Not Yet Known

Ref	Description	Estimated Range	Notes
U1	Electrical works	£TBC	New circuits, sockets, dedicated supply for equipment — requires electrician survey
U2	Structural / building works	£TBC	Depends on condition survey of existing room
U3	Painting and decoration	£TBC	Possibly in-house; if contractor, needs quote
U4	VAP shipping (to Bristol and back)	£TBC	Logistics to be arranged by Tugboat & Dolphins / DHR
U5	iPad/tablet provision	£TBC	May already be available; if not, allow ~£300–£500
U6	Removal and disposal of existing equipment	£TBC	Skip hire, contractor labour
U7	Project management	£TBC	If Wayne Fulton manages in-house — no direct cost; if external, needs budget
U8	Contingency (recommended 10–15%)	~£1,656–£2,484	Based on current known costs
U9	VAT on all quotes	£TBC	Quotes do not explicitly state ex-VAT or inc-VAT — clarification required
Total Unknown Costs		Unknown	

4.4 Estimated Total Project Cost (with Contingency)

	Low Estimate	High Estimate
Confirmed quotes	£16,560	£16,560
Electrical works	£1,000	£3,000
Building / decorating	£500	£2,000
VAP shipping	£200	£500
iPad/tablet	£0 (if available)	£500
Equipment disposal	£200	£600
Contingency (10%)	£1,846	£2,316
Estimated Total	~£20,306	~£25,476

⚠ VAT position is unknown — if quotes are ex-VAT, 20% VAT would increase costs by up to ~£3,312 on confirmed quotes alone. **This must be clarified as a priority.**

5. Contractor Breakdown

5.1 Primary Contractor — So Sensory

Detail	Information
Company	So Sensory
Website	www.sosensory.com
Contact	Kevin Phillips (kevin.phillips@sosensory.com)
DHR Contact	Wayne Fulton
Scope	Sensory equipment, lighting, projector, AV, floor & wall padding, Bluetooth controls
Payment Terms	50% deposit on order; balance on completion
Warranty	5-year full service warranty on projector equipment
Quotes Ref	180326, 200326, 210326

5.2 Sub-Contractor — Tugboat & Dolphins

Detail	Information
Company	Tugboat & Dolphins
Location	Plymouth
DHR Contact	Jorden Kelevra
Scope	Vibro Acoustic Platform (VAP) foam covering
Factory Location	Bristol (for covering work)
Estimate Ref	E190326
Notes	Electronics must be removed before shipping; shipping costs not included

5.3 Contractors Still Required (TBC)

Contractor Type	Scope	Status
Electrician	Survey existing electrical installation, install new circuits/ sockets, sign off	Not yet identified
Decorator / Painter	Prepare and paint/finish walls and ceiling if required	Not yet identified (possibly in-house)
Building / Joinery Contractor	Any structural modifications, door adjustments, ceiling repairs	Not yet identified — depends on condition survey
Logistics / Transport	Shipping of VAP to/from Bristol factory	Not yet arranged

6. In-House vs Contractor Work

Task	In-House	Contractor	Notes
Project management and co-ordination	✓ Wayne Fulton		
Obtain and review further quotes	✓ Wayne Fulton		
Room condition survey / pre-works inspection	✓ Facilities team		
Electrical survey and works		✓ Electrician	Needs to be arranged
Removal and disposal of old equipment	✓ Maintenance team (if light)	✓ Contractor (if heavy/specialist)	Assess on site
Structural / building repairs		✓ Building contractor	Only if required
Painting and decoration	✓ Maintenance team (if resourced)	✓ Decorator (if required)	To decide
Sensory equipment install		✓ So Sensory	Labour included in Q1
Projector & AV install		✓ So Sensory	Included in Q2
Floor and wall padding install		✓ So Sensory	Included in Q3
VAP foam covering		✓ Tugboat & Dolphins	Estimate received
VAP logistics / shipping	✓ Co-ordinate (Wayne)	✓ Transport company	To arrange
IT setup (iPad, network)	✓ IT team (software)	✓ So Sensory (hardware)	iPad availability TBC
Snagging and final inspection	✓ Wayne Fulton / Facilities		
Funding management and reporting	✓ Finance / Trustees		


7. Project Timeline — Gantt Chart

⚠ Note: Exact dates are not confirmed. The timeline below is a **proposed draft** based on typical project timescales. Start date, key milestones and completion date all need to be confirmed. All quotes are dated March 2026.

Phase Overview

Phase	Description	Estimated Duration
Phase 0	Information gathering and gap-filling	2 weeks
Phase 1	Planning and approvals	2 weeks
Phase 2	Pre-works (electrical, structural, removal)	2–3 weeks
Phase 3	Main installation works	2–3 weeks
Phase 4	Finishing, snagging and commissioning	1–2 weeks
Total		~9–12 weeks from approval

Draft Gantt Chart

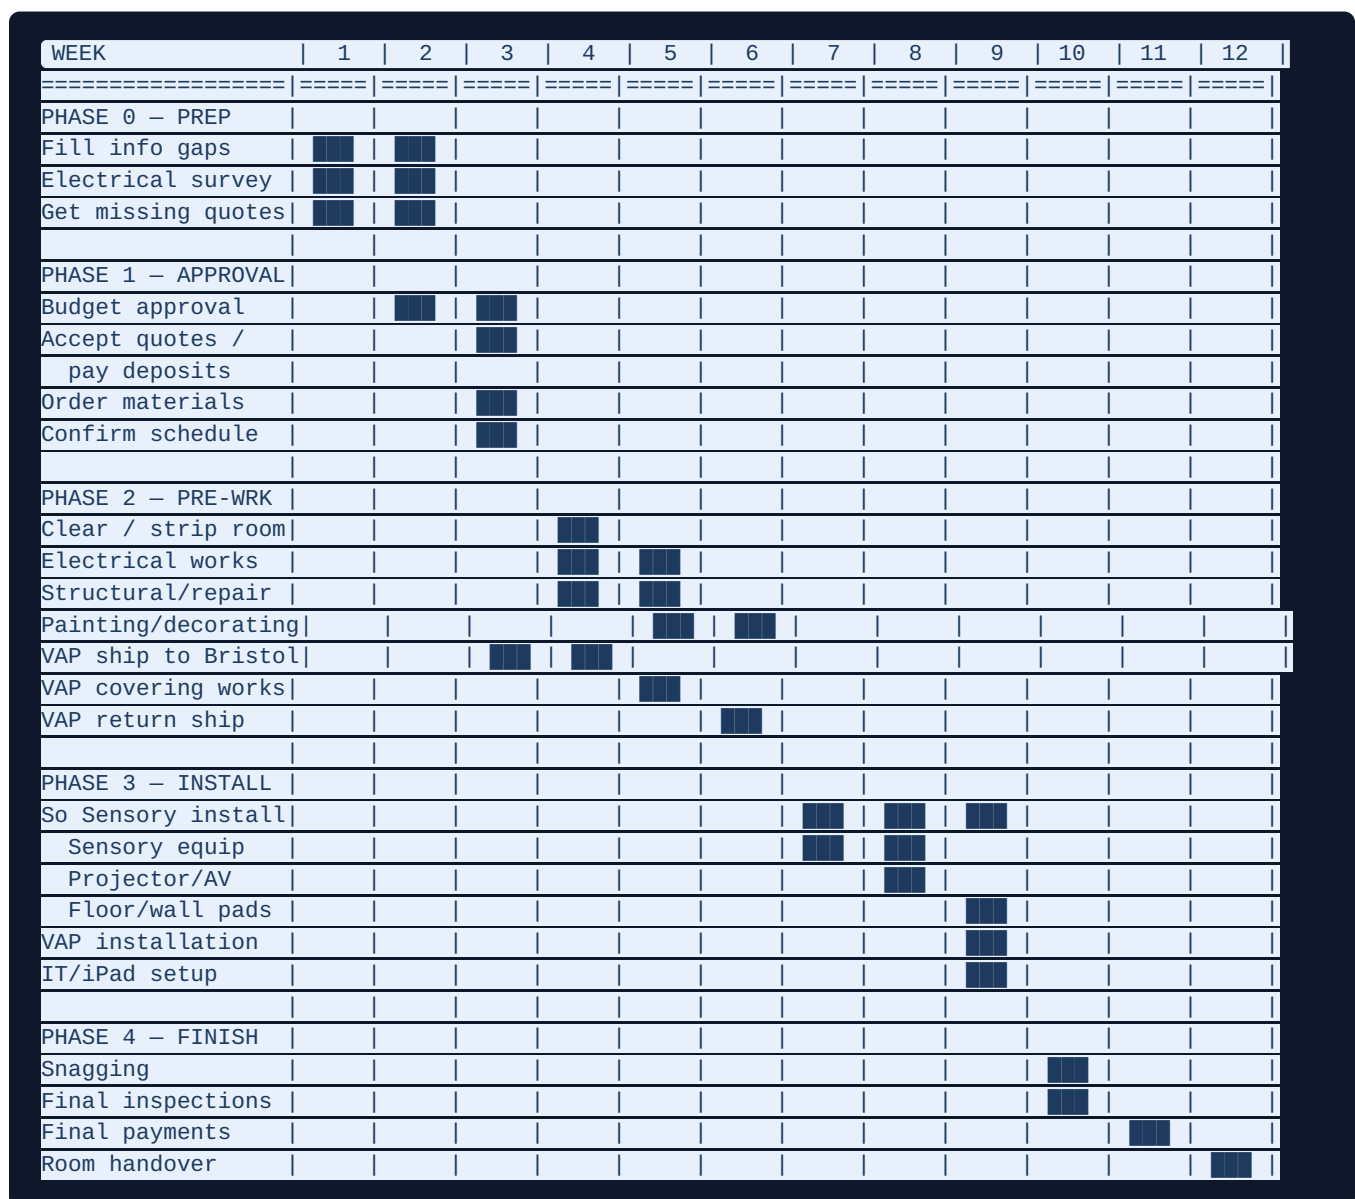

Key dependency: So Sensory installation (Phase 3) cannot start until pre-works (Phase 2) are complete. VAP covering must be complete and shipped back before installation day.

Key Milestones

Milestone	Target Week	Owner
All information gaps resolved	Week 2	Wayne Fulton
Full project budget approved	Week 3	Trustees / Finance
Deposits paid and works ordered	Week 3	Wayne Fulton
Pre-works complete (electrical, structural, decorating)	Week 6	Facilities Manager
VAP returned from Bristol	Week 6	Wayne Fulton / Logistics
So Sensory installation complete	Week 9	So Sensory / Wayne Fulton
Snagging and sign-off complete	Week 10	Wayne Fulton
Room open to users	Week 12	Dame Hannah Rogers Trust

8. Funding Breakdown

⚠ The source and total amount of funding is not yet documented in the available files. The following is a template to be completed once funding details are confirmed.

8.1 Funding Sources (To Be Confirmed)

Source	Type	Amount Confirmed	Amount Pending	Notes
[Donation — name TBC]	Donation	£TBC	£TBC	Referenced in problem statement as "a donation to refurbish the sensory room"
[Grant — name TBC]	Grant	£TBC	£TBC	To be confirmed
Internal Budget	DHR Budget	£TBC	£TBC	To be confirmed
Total Funding		£TBC	£TBC	

8.2 Funding vs Expenditure Summary (To Be Completed)

Category	Budget Allocated	Estimated Cost	Variance
Sensory equipment (So Sensory Q1)	£TBC	£8,525.00	£TBC
Projector & AV (So Sensory Q2)	£TBC	£2,495.00	£TBC
Floor & wall padding (So Sensory Q3)	£TBC	£5,000.00	£TBC
VAP covering (Tugboat & Dolphins)	£TBC	£540.00	£TBC
Electrical works	£TBC	£TBC	£TBC
Structural / decorating	£TBC	£TBC	£TBC
Logistics / shipping	£TBC	£TBC	£TBC
iPad / tablet	£TBC	£TBC	£TBC
Contingency (10%)	£TBC	~£1,850–£2,500	£TBC
Total	£TBC	~£20,000–£25,000	£TBC

9. Risk Register

Risk	Likelihood	Impact	Mitigation
Quotes do not include VAT — actual cost higher than expected	Medium	High	Clarify VAT position with So Sensory immediately
Funding insufficient to cover full project cost	Medium	High	Confirm total funding available before accepting any quotes
Electrical survey reveals significant additional works needed	Medium	High	Commission electrical survey in Phase 0 before committing to timeline
VAP shipping delayed — delays Phase 3 installation	Medium	Medium	Arrange shipping as early as possible once VAP is ready
Room not available during works — impact on current users	High	Medium	Plan decant of current users; communicate in advance
iPad/tablet not available — Bluetooth controls cannot be set up	Low	Medium	Confirm availability with IT team; budget for purchase if needed
Key contractor (So Sensory) unavailable at required time	Low	High	Agree schedule in writing as soon as possible after deposit
Structural issues found once room is stripped	Low	High	Allow contingency budget; get structural survey if room is old
Quote validity expires — prices may change	Medium	Medium	So Sensory quotes dated 18 March 2026 — confirm validity period
Donor conditions not met — funding at risk	Low	High	Clarify any conditions attached to the donation

10. Gaps — What We Don't Know and Need to Find Out

This section is **critical**. The following information is **missing** and must be resolved before the project can proceed to formal approval and execution.

10.1 Funding and Financial

#	Gap	Action Required	Priority
F1	Total donation / funding amount available	Confirm with Finance/Trustees — how much has been donated and is it ring-fenced for this project?	● Critical
F2	Are there any conditions attached to the donation? (e.g. donor requirements, restricted use, reporting obligations)	Check with Finance/Fundraising team	● Critical
F3	Are the So Sensory quotes inclusive or exclusive of VAT?	Email Kevin Phillips at So Sensory to clarify — this could add ~£3,312 to confirmed quote costs alone	● Critical
F4	Is VAT reclaimable by Dame Hannah Rogers Trust?	Confirm with Finance team — charitable status affects VAT position	● Critical
F5	Is there any internal DHR budget contribution?	Confirm with Finance	● High
F6	Are there any grant funding opportunities that could supplement the donation?	Check with Fundraising team	● High

10.2 Scope and Technical

#	Gap	Action Required	Priority
T1	Current condition of the sensory room — full survey not documented	Commission a pre-works survey including electrical, structural and decorative condition	 Critical
T2	Electrical requirements — no electrical survey or quote	Appoint a qualified electrician to survey and quote for any new circuits, dedicated supplies, socket positions	 Critical
T3	Is the iPad/tablet available for the room?	Confirm with IT team — required for Bluetooth switching controls (So Sensory Quote 1 assumption)	 Critical
T4	Are the 3D drawings final and approved?	Confirm with So Sensory that drawings match the agreed scope	 High
T5	Does the VAP already exist / what is its current status?	Clarify with Wayne Fulton — is it already constructed? Where is it? Is it owned by DHR?	 Critical
T6	VAP shipping logistics and cost	Arrange transport quote for Ivybridge to Bristol (to Tugboat & Dolphins factory) and return	 High
T7	Network infrastructure — is there an ethernet point in the room?	Check with IT team; So Sensory quote includes WiFi/ ethernet adapter but network point may be needed	 High
T8	Removal and disposal of existing room equipment and furnishings	Identify what is currently in the room; assess what can be donated, stored or disposed of	 High
T9	Any structural or building works required	Identify from condition survey; arrange quotes if needed	 High
T10	Painting and decoration requirements	Identify from condition survey; confirm whether in-house or contractor	 Medium

10.3 Programme and Planning

#	Gap	Action Required	Priority
P1	Project start date	Agree with Trustees and Wayne Fulton once funding is confirmed	 Critical
P2	Target completion date	Agree with Trustees — is there a deadline driven by the donation or other commitment?	 Critical
P3	Quote validity periods — So Sensory quotes are dated March 2026	Confirm with Kevin Phillips how long the quotes are valid for	 High
P4	So Sensory availability — when can they schedule the works?	Contact So Sensory to confirm earliest installation window	 High
P5	Room availability — when can the room be taken out of use?	Confirm with care/services team — how will current users be affected and what is the decant plan?	 High
P6	Who is the formal Project Manager?	Confirm — assumed Wayne Fulton but needs to be formally designated	 High

10.4 Compliance and Governance

#	Gap	Action Required	Priority
C1	Trustee/Board approval — has this project been formally approved?	Check governance requirements; obtain formal approval before committing expenditure	 Critical
C2	Any planning permission or building control required?	Check with Local Authority if structural or significant cosmetic changes are involved	 High
C3	Fire safety compliance — do new floor/wall padding materials meet fire safety standards?	Confirm with So Sensory that materials comply with applicable fire safety regulations (BS 7176 etc.)	 High
C4	Health and Safety during works — is there a Construction Phase Plan required?**	If works value exceeds CDM threshold (~£500 specific criteria), a CPP may be required	 High
C5	Contractor compliance checks — have So Sensory and Tugboat & Dolphins provided insurance and accreditation?**	Request copies of Public Liability Insurance, relevant accreditations	 High
C6	Electrical installation certificate — will a BS 7671 certificate be issued?	Confirm with electrician that all electrical works will be certified	 High

10.5 Operational

#	Gap	Action Required	Priority
O1	Communication plan for residents / families	Inform relevant residents, families and staff of disruption during works	 High
O2	Staff training for new equipment	Arrange training with So Sensory for staff on using new Bluetooth controls, projector, etc.	 Medium
O3	Maintenance plan for new equipment	So Sensory provide 5yr warranty on projector; confirm maintenance arrangements for all other items	 Medium
O4	Warranty documentation	Ensure all warranties are documented and stored	 Medium

11. Next Steps & Action List

The following actions are required immediately to move the project forward:

#	Action	Owner	Deadline	Status
1	Confirm total funding amount and any donor conditions	Finance / Trustees	ASAP	☐ To Do
2	Clarify VAT position on all So Sensory quotes (inc. or ex. VAT?)	Wayne Fulton / Finance	ASAP	☐ To Do
3	Obtain formal Trustee/Board approval for the project and budget	Wayne Fulton / CEO	Week 1–2	☐ To Do
4	Confirm validity period of all So Sensory quotes	Wayne Fulton → Kevin Phillips	Week 1	☐ To Do
5	Commission electrical survey of existing sensory room	Wayne Fulton → Electrician	Week 1–2	☐ To Do
6	Commission full pre-works condition survey of room	Wayne Fulton / Facilities	Week 1–2	☐ To Do
7	Confirm current status and location of the VAP	Wayne Fulton	Week 1	☐ To Do
8	Arrange transport quote for VAP to/from Bristol	Wayne Fulton	Week 1–2	☐ To Do
9	Confirm iPad/tablet availability with IT team	Wayne Fulton → IT	Week 1	☐ To Do
10	Confirm So Sensory availability for installation	Wayne Fulton → Kevin Phillips	Week 2	☐ To Do
11	Identify and quote additional contractors (electrician, decorator, structural if needed)	Wayne Fulton	Week 2–3	☐ To Do
12	Confirm room availability / plan for current users during works	Wayne Fulton → Care/ Services	Week 2	☐ To Do
13	Confirm fire safety compliance of padding materials	Wayne Fulton → So Sensory	Week 2	☐ To Do
14	Request copies of contractor insurance and accreditations	Wayne Fulton	Week 2–3	☐ To Do
15	Pay deposits and formally accept quotes (once all above resolved)	Wayne Fulton / Finance	Week 3	☐ To Do
16	Agree formal project schedule with all contractors	Wayne Fulton	Week 3	☐ To Do
17	Arrange staff communication and resident/family notification	Wayne Fulton / Care team	Week 3	☐ To Do

Appendix A — Document Reference List

Document	File	Date
Sensory Equipment Upgrade Quote (Ref 180326)	Dame Hannah Rogers v3.0.pdf	18 March 2026
Floor & Wall Padding Quote (Ref 200326)	DHR-Floor & Wall Panels Quotation.pdf	18 March 2026
HD Projector Quote (Ref 210326)	DHR-Projector Sensory Room Quotation.pdf	18 March 2026
VAP Covering Estimate (Ref E190326)	VAP estimate Tugboat & Dolphins.pdf	18 March 2026
3D Representation Drawings	Dame Hannah Rogers Trust 3D Dwgs.pdf	March 2026

This document was prepared to collate all available project information and identify gaps. It is a working draft and should be updated as further information is obtained. Once all gaps are resolved, this document should be updated to form the final approved Project Plan.
